


LaOtto ADA Ramps – 2023 Project



LAOTTO SIDEWALKS

The scope of work for the 2023 ADA project was the replacement of sidewalks and ramps with new ADA compliant facilities at Section 12 through 15 in the Town of LaOtto.

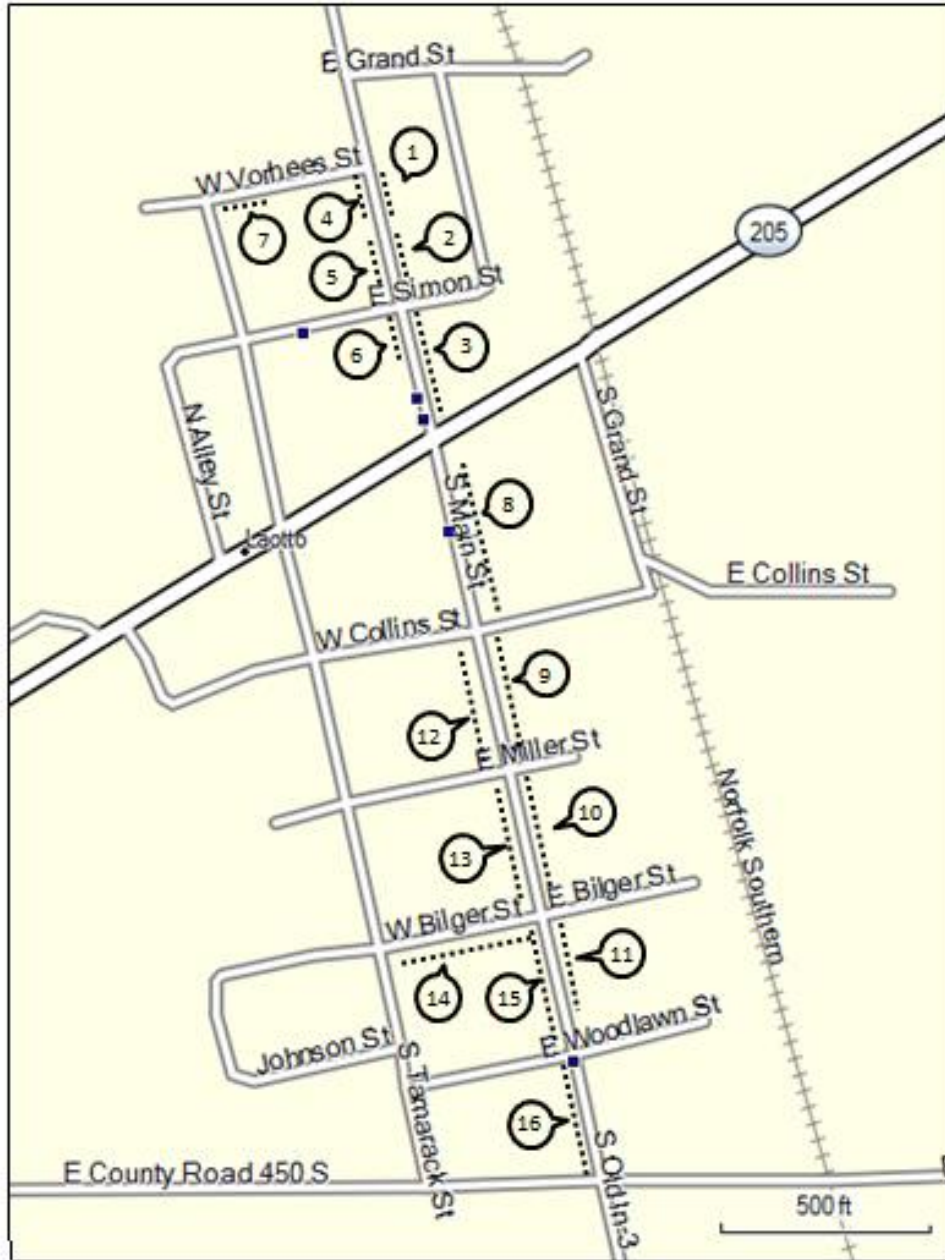

Section 12



Miller Street (Section 12 to 13 Transition)



Section 13



Bilger Street (Section 13 to 15 Transition)



Section 15



Woodlawn Street (End of Section 15)

Cobblestone ADA Ramps – 2022 Projects



The scope of work for the 2022 ADA project was install ADA compliant ramps at 3 additional locations in the Cobblestone subdivision to bring the sidewalks up to compliance with ADA.

Additionally, sidewalk repairs were made on Bridge 1 in Ligonier.



Ramp - 6C



Ramp - 7A



Ramp - 7B



Bridge 1 - Before



Bridge 1 - After

Cobble Stone ADA Ramps - Project 2020



The scope of work for the 2020 ADA project was install ADA compliant ramps at 7 locations throughout the Cobblestone subdivision to bring the sidewalks up to compliance with ADA.



1A – Cobblestone Lane



1B – Cobblestone Lane



2A – Laurelwood Lane



2B – Laurelwood Lane



3A – Cobblestone Lane



3B – Cobblestone Lane



4 – Ballenshire Lane



4 – Ballenshire Lane



5 – Carnoustie Circle



5 – Carnoustie Circle



7A – Carnoustie Circle



7B – Carnoustie Circle

CR 1000 East Sidewalk Project 2019



The sidewalks north and south of the Kendallville Outdoor Recreation Complex on CR 1000 East were repaired in 2019. The existing sidewalks were installed to ADA standards when Bridge 5 was reconstructed in 2008. However, preventive maintenance was required to keep the sidewalks in good working order. Cleaning, crackfill/crackseal of joints and minor patching repairs were performed on approximately 1950' of sidewalks.



Crackfill / Crackseal



Crackfill / Crackseal (sidewalk joint)



Patching / Minor Repair



CR 1000 East looking south at Bodenhafer Drive



CR 1000 East looking north at Complex Entrance



CR 1000 East at Complex Entrance looking north



CR 1000 East looking north at Bridge 5



Repairs on Bridge 5 sidewalk



CR 1000 East on Bridge 5 looking north

Appendix A - LaOtto Sidewalk Project 2018

Old State Road 3, north of SR 205



The sidewalks north of SR 205 in LaOtto were replaced in 2018. The old sidewalks were removed and new sidewalk that meet ADA standards were installed. Approximately 975' feet of 5' feet wide sidewalk was replaced, along with the addition of five new ADA ramps. There was also a 50' section of building adjacent heaved sidewalk, just south of Collins street on the Westside of SR 205 that was replaced.



At Simon Street looking South (Eastside)



At Simon Street looking North (Eastside)



At Simon Street looking North (Westside)



At Vorhees Street looking South (Eastside)



At Vorhees Street looking South (Westside)



North of SR 205 looking South (Westside)



South of Collins street on the Westside of SR 205 looking North

Appendix A - 2017 ADA Project

Wolf Lake Sidewalk Improvements

Wolf Lake Street from U.S. 33 to Main Street

Pulver and Sons from Albion removed approximately 300' feet of old sidewalk and replaced with new concrete, the new sidewalk is 5' feet wide with an ADA mat at the Main Street intersection. The work began on August the 14th with the removal of the old sidewalk, the new concrete was poured on August the 15th. The edge work and seeding was completed on September the 13th. This updated sidewalk provides a new, smooth, ADA compliant sidewalk from the pedestrian crosswalk at U.S. 33 to the elementary school at Wolf Lake.





Photos of existing conditions taken summer of 2017 before work began.



Forms were set and concrete poured on August the 15th.



August the 16th day after concrete was poured.



September 14th day after seeding.

Appendix A - 2016 ADA Project

Wawaka Sidewalk Improvements



The Wawaka sidewalk project was completed in 2016. These sidewalks are located on the west side of Albion street starting at U.S. 6 and proceeding North to Depot street. The second would be on the South side of Depot street starting at Albion street and going west for 120'. The total distance is estimated at 540' with four ramps. All of the existing sidewalks were at a D rating. The trees were removed, stumps were ground, and the old sidewalk was removed. Edsall Construction of Albion poured the sidewalk and ADA ramps. A total of four ADA ramps were installed, and 520' feet of sidewalk was poured at a costs of \$14,720. This finished project increases the sidewalk ratings to an "A" grade, which brings the area into compliance with ADA requirements.

ADA Sidewalk, Wawaka 2016



Before construction began



ADA Sidewalk, Wawaka 2016



After Tree removal and stump grinding



ADA Sidewalk, Wawaka 2016



Concrete Poured



Concrete Poured



Sidewalk Complete

July 21, 2016





Asphalt was placed to match the concrete to the road.

The finished product.
